

 **PROVIDENT**
ADORA DE GOA

Construction Updates

December 2024




Dear Esteemed Customer,

Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Adora de Goa. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

*We are grateful for your kind cooperation.
Team Provident Adora de Goa*

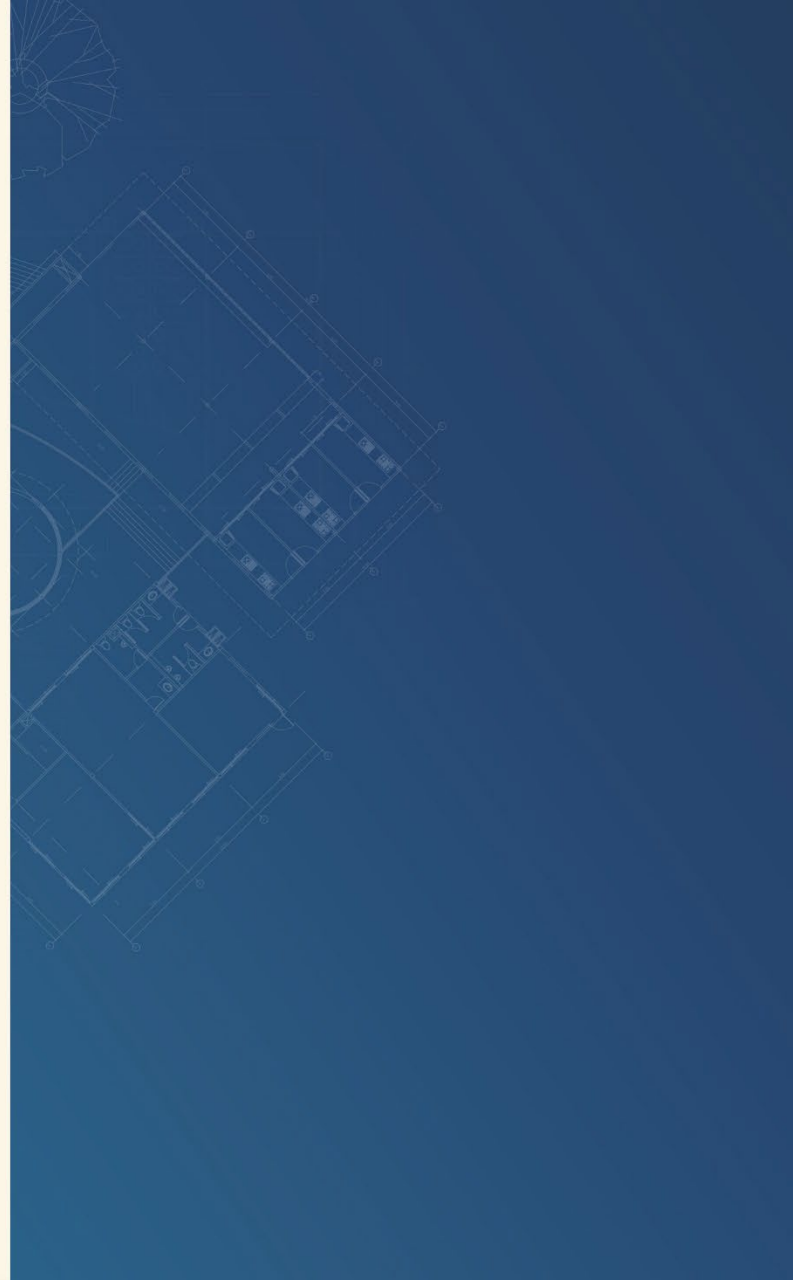



Provident Adora de Goa

Dabolim at Central Goa



Construction Updates

Overall view

Row 18



TOWER STATUS

- Customer inspection in progress.

PROGRESS TIMELINE



Actual site photograph


Row 17



TOWER STATUS

- Customer inspection in progress.

PROGRESS TIMELINE



September 24

October 24

November 24

December 24

Row 16



TOWER STATUS

- Snag works in progress.

PROGRESS TIMELINE



Actual site photograph

Row 15



TOWER STATUS

- Snag works in progress.

PROGRESS TIMELINE



Actual site photograph

Row 14



TOWER STATUS

- Snag works in progress.

PROGRESS TIMELINE



September 24

October 24

November 24

December 24

Row 13



TOWER STATUS

- Snag works in progress.

PROGRESS TIMELINE




September 24



October 24



November 24



December 24


Row 12



TOWER STATUS

- Customer inspection in progress.

PROGRESS TIMELINE



September 24

October 24

November 24

December 24

Row 11



TOWER STATUS

- Customer inspection in progress.

PROGRESS TIMELINE



September 24

October 24

November 24

December 24

Row 10



TOWER STATUS

- Customer inspection in progress.

PROGRESS TIMELINE



September 24

October 24

November 24

December 24

Row 9



TOWER STATUS

- Row 9A,B&C above terrace works in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Row 9A,B & C terrace slab completed.
- Row 9A,B & C structure completed.



UPCOMING CONSTRUCTION MILESTONES

- Row 9A waterproofing work to be start.

PROGRESS TIMELINE



September 24

October 24

November 24

December 24

Row 8



TOWER STATUS

- Row 8A flooring work & structural steel work in progress.
- Row 8B structural steel & waterproofing work in progress.
- Row 8C structural steel work in progress.
- Row 8D above terrace work & structural steel work in progress.
- Row 8 flooring work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Row 8A,B,C&D Terrace slab completed.



UPCOMING CONSTRUCTION MILESTONES

- Row 8A completion of flooring work.
- Row 8B completion of waterproofing works and wall dado works.

PROGRESS TIMELINE



September 24

October 24

November 24

December 24

Row 7



TOWER STATUS

- Row 7A wall tiles dado work in progress.
- Row 7A balcony railing work in progress
- Row 7C waterproofing work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Row 7A,B,C&D terrace slab completed.
- Row 7B up to three floors waterproofing works completed.
- Row 7A sunken filing work completed.



UPCOMING CONSTRUCTION MILESTONES

- Row 7A tile flooring work to start.
- Row 7B wall tile dado work to start.

PROGRESS TIMELINE



September 24


October 24

November 24

December 24

Actual site photograph

Row 6

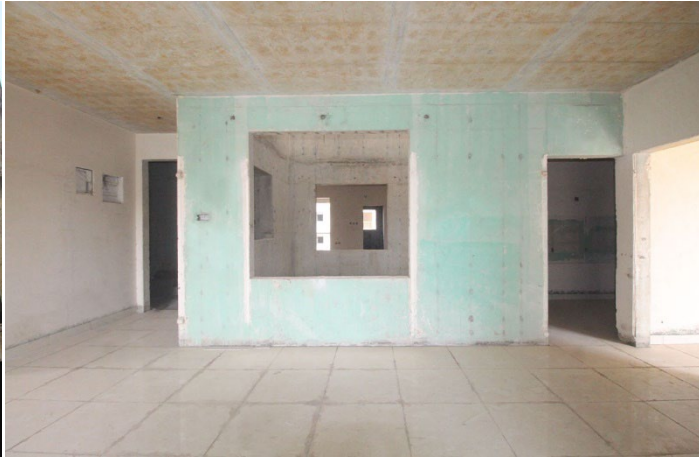

TOWER STATUS

- Row 6C waterproofing & sunken filling & tiling work in progress.
- Row 6E waterproofing work in progress.
- Row 6C railing work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Row 6A,B,C&D terrace slab completed.



UPCOMING CONSTRUCTION MILESTONES

- Row 6A,B,C & E tile flooring and wall dado works to start.

PROGRESS TIMELINE



September 24

October 24

November 24

December 24

Row 5



TOWER STATUS

- Row 5A terrace sloped roof work in progress.
- Row 5B common area flooring, terrace sloped roof work in progress.
- Row 5C common area flooring work & terrace sloped roof work in progress.
- Row 5D terrace sloped roof work in progress.
- Row 5D vitrified flooring work in progress
- Row 5A fixing of windows work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Row 5A,B,C&D terrace slab completed.
- Row 5C gypsum work completed.
- Row 5A,B&C vitrified flooring completed.
- Row 5A,B&C external plumbing work completed.



UPCOMING CONSTRUCTION MILESTONES

- Row 5D completion of flooring & windows work.

PROGRESS TIMELINE



September 24

October 24

November 24

December 24

Row 4



TOWER STATUS

- Row 4A,B & C floor tiling work in progress.
- Row 4C wall tile dado and waterproofing work in progress.
- Row 4D waterproofing work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Row 4A,B,C&D terrace slab completed.
- Row 4A,B,C & D gypsum work completed.
- Row 4A & 4B external plumbing work completed.



UPCOMING CONSTRUCTION MILESTONES

- Row 4A,B,C & D railing work to start.
- Row 4C completion of wall dado and floor tiling work.

PROGRESS TIMELINE



September 24



October 24



November 24



December 24

Row 3



TOWER STATUS

- Row 3A dado work in progress.
- Row 3B dado Work in progress.
- Row 3C Tiling work in progress.
- Row 3A,B,C&D railing work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Row 3A,3B,3C & 3D terrace waterproofing work completed.
- Row 3A & B flooring work completed.
- Row 3A, 3B, 3C & 3D external plumbing, terrace waterproofing completed.



UPCOMING CONSTRUCTION MILESTONES

- Row 3C & D flooring work completion.
- Row 3A,B,C & D windows completion.

PROGRESS TIMELINE



Actual site photograph

Row 2



TOWER STATUS

- Row 2B railing and flooring work in progress.
- Row 2A & B fixing of windows work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Row 2A internal door fixing work completed.
- Row 2A & 2B external plumbing, terrace waterproofing completed.



UPCOMING CONSTRUCTION MILESTONES

- Row 2A balcony railing work completion.
- Flooring & dado work completion.

PROGRESS TIMELINE



September 24

October 24

November 24

December 24

Actual site photograph

Row 1



TOWER STATUS

- Row 1A & 1B terrace & balcony railing work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Row 1A&B terrace slab completed.
- Row 1B gypsum plastering work in progress.



UPCOMING CONSTRUCTION MILESTONES

- Row 1A&B balcony railing work completion.

PROGRESS TIMELINE



September 24

October 24

November 24

December 24

Actual site photograph

Mixed – Use Commercial



TOWER STATUS

- MUC – 2nd slab for pour 1 completed.
- MUC – 2nd slab for pour 2 completed.
- MUC – 2nd to 3rd floor column pour 2 work in progress.

PROGRESS TIMELINE



Actual site photograph

Other activities

Overall view



Blu area



TOWER STATUS

- Club house - completed.
- DG & transformer fixed - cable work in progress for phase 2.
- Road work - WMM, PCC & pavers work in progress for phase 2.
- Services – MEP works in progress for phase 2.

PROGRESS TIMELINE



September 24

October 24

November 24

December 24

Contact Us



Site Office :

Provident Adora de Goa

Sy.No.198, Zuari Nagar, Vidhyanagar Colony, Chicalim, Goa – 403726.

Regional Office :

Provident Housing Limited

No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-44555544

Email : crm@providenthousing.com (Subject line – Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.providenthousing.com

RERA Registration Number :

RERA No.: PRGO02190645 (ROW 5 & 6)

RERA Nos.: PRGO02180009 (Row 10,11 & 12), PRGO07180544 (Row 13)

PRGO07180560 (Row 14), PRGO07180561 (Row 15)
