

 **PROVIDENT**
CAPELLA

Construction Updates

September 2024



Dear Esteemed Customer,


Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Capella. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation.

Team Provident Capella

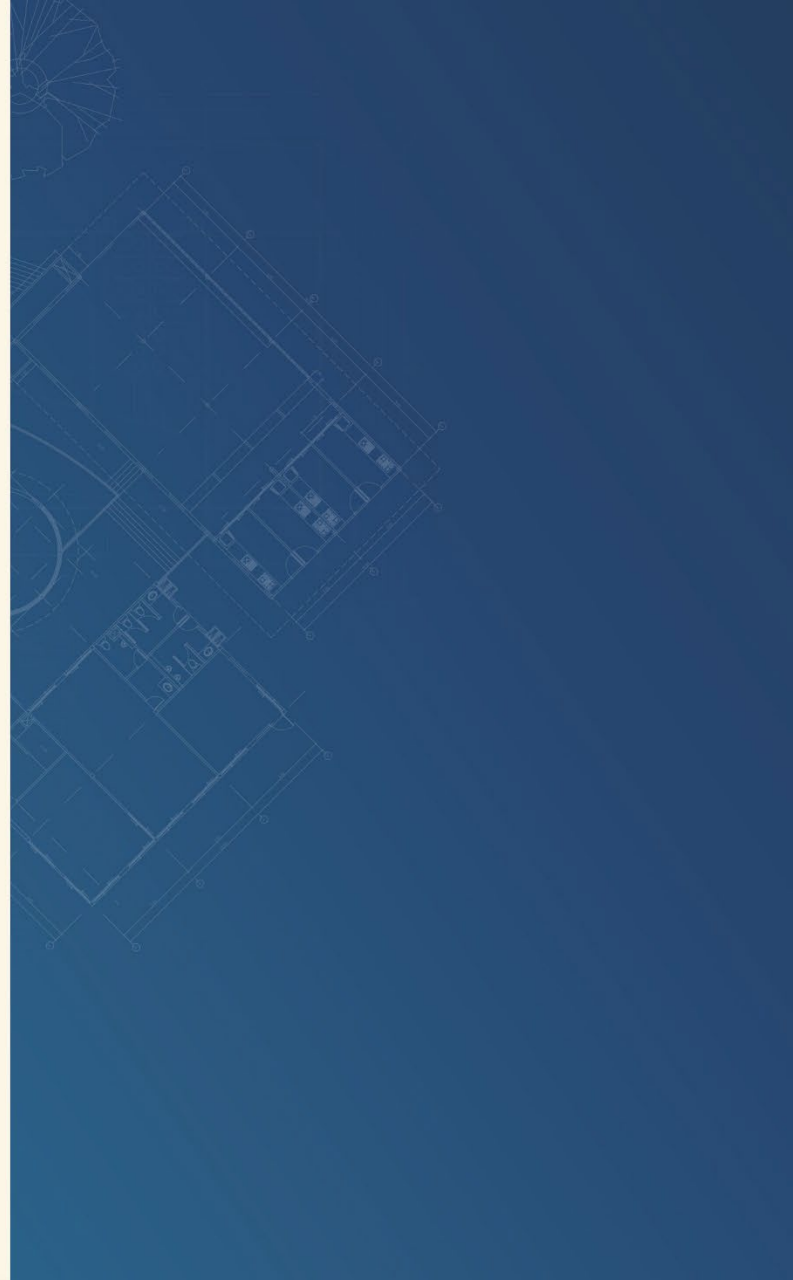



Provident Capella

Whitefield, Bengaluru



Construction Updates

Overall view

Tower 1



Actual site photograph



TOWER STATUS

- 11th - 12th floor tile work in progress.
- 3rd – 12th floor water proofing work completed.
- 3rd – 12th WP & balcony railing work completed.
- 2nd - 12th MS framework at kitchen completed
- 11th & 12th floor wooden doors installation work in progress.
- Lift installation completed.
- Terrace water proofing completed.
- 3rd – 4th floor internal electrical completed, 5th floor work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- 3rd - 10th floor tile work completed.
- 3rd - 12th UPVC windows completed.
- 3rd - 10th floor wooden doors completed.



UPCOMING CONSTRUCTION MILESTONES

- 11th – 12th floor tile work completion.
- 11th - 12th floor wooden door completion.

PROGRESS TIMELINE



June 24

July 24

August 24

September 24

Tower 2



Actual site photograph



TOWER STATUS

- External texture paint completed up to 1 coat, final coat pending.
- 3rd - 8th floors internal flat painting completed; 9th floor work in progress.
- 3rd – 12th floor fire door installation completed.
- VDF flooring at car parking at basement completed, 1st floor IPS flooring completed.
- 3rd – 7th floor lobby finishing work completed, 8th – 12th floors work in progress.
- 3rd – 11th floor internal flat electrical work completed; 12th floor work in progress.
- 3rd – 9th floor CP sanitary completed.



CONSTRUCTION MILESTONES ACHIEVED


- 2nd - 12th flooring work completed.
- 3rd - 12th floor UPVC window installation completed.
- 3rd - 12th floor doors installation completed.
- Lift installation completed.



UPCOMING CONSTRUCTION MILESTONES

- 2nd floor doors installation.
- 2nd floor windows installation.

PROGRESS TIMELINE



June 24

July 24

August 24

September 24

Tower 3



Actual site photograph



TOWER STATUS

- 3rd - 12th floor internal flat electrical work completed, 2nd floor work in progress.
- 3rd - 12th floor CP sanitary fittings completed, 2nd floor work in progress.
- 3rd – 11th floors internal painting completed; 12th floor work in progress.
- External texture paint first coat completed, final to be done later.
- Ground floor 1st coat paint completed.
- VDF flooring at car parking at basement completed, 1st floor IPS completed.
- Lobby wall putty completed; 12th floor painting work in progress.



CONSTRUCTION MILESTONES ACHIEVED


- 2nd - 12th flooring work completed.
- 3rd – 12th floor UPVC window installation completed.
- 3rd – 12th floor door installation completed.
- Lift installation completed.



UPCOMING CONSTRUCTION MILESTONES

- 2nd floor doors installation.
- 2nd floor windows installation.

PROGRESS TIMELINE



June 24

July 24

August 24

September 24

Tower 4



Actual site photograph



TOWER STATUS

- 3rd – 12th floor gypsum & balcony railing completed.
- 3rd – 7th internal painting completed; 8th floor work in progress.
- 3rd – 12th floor water proofing completed.
- Staircase 01 railing completed, S-02 work in progress.
- 3rd -12th kitchen granite completed.
- Terrace waterproofing completed.
- External painting work in progress.
- 3rd - 5th floor internal flat electrical completed.
- 3rd floor CP sanitary fittings completed; 4th floor work in progress.



CONSTRUCTION MILESTONES ACHIEVED


- 3rd - 12th floor flooring completed.
- 3rd – 11th floor wooden doors installation completed.
- 3rd – 12th floor UPVC windows installation completed.
- Lift installation completed.



UPCOMING CONSTRUCTION MILESTONES

- 2nd floor flooring work completion.
- 2nd & 12th floor wooden door installation.

PROGRESS TIMELINE



June 24

July 24

August 24

September 24

Tower 5



Actual site photograph



TOWER STATUS

- 3rd – 12th water proofing & balcony railing work completed.
- 2nd - 12th MS framework at kitchen completed.
- 2nd - 12th gypsum work completed.
- External texture painting work in progress.
- Staircase railing work in progress.
- Lift installation completed.
- Grouting & deep cleaning work in progress.
- 3rd – 6th floor CP sanitary fittings completed.
- 3rd – 8th floor internal flat electrical work completed, 9th – 12th floor work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- 2nd - 12th floor tile work completed.
- 3rd - 12th upvc windows completed.
- 3rd – 12th floor wooden door completed.
- Lift installation completed.



UPCOMING CONSTRUCTION MILESTONES

- 2nd floor wooden door installation.
- 2nd floor UPVC windows installation.

PROGRESS TIMELINE



June 24

July 24

August 24

September 24

Tower 6



Actual site photograph

TOWER STATUS

- 3rd – 7th floor tile work completed.
- Balcony railing completed.
- 3rd – 10th floor gypsum plastering work completed, 11th – 12th floor work in progress.
- Toilet water proofing completed.
- 3rd – 9th floor staircase railing completed.
- Above terrace work in progress.
- 3rd -12th gypsum plaster completed.



CONSTRUCTION MILESTONES ACHIEVED

- Roof slab concrete completed.
- 3rd – 7th floor tile work completed.



UPCOMING CONSTRUCTION MILESTONES

- 7th – 9th floor flooring completion.

PROGRESS TIMELINE



June 24

July 24

August 24

September 24

Tower 7



Actual site photograph

TOWER STATUS

- 9th floor roof slab completed.
- Terrace floor slab work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- 9th floor roof slab completed.



UPCOMING CONSTRUCTION MILESTONES

- Terrace floor slab completion.

PROGRESS TIMELINE



June 24

July 24

August 24

September 24

Other Activities

Basement



Driveway



ACTIVITY STATUS

- 625 KV DG set commissioning completed.
- STP mechanical commissioning completed.
- Fire pump room commissioning completed.
- WTP ready for commissioning.
- OWC equipment completed.
- Car parking marking in progress.
- Clubhouse interior work in progress.
- Clubhouse external wall cladding work in progress.
- East & south side compound wall completed.
- Driveway work in progress.
- Hardscapes work in progress.

PROGRESS TIMELINE



June 24

July 24

August 24

September 24

Contact Us



Site Office :

Provident Capella

Whitefield, Soukya Rd, Bengaluru, Karnataka 562114

Regional Office :

Provident Housing Limited

No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-44555544

Email : crm@providenthousing.com (Subject line – Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.providenthousing.com

RERA Registration Number :

RERA Nos.: PRM/KA/RERA/1250/304/PR/190606/002596

PRM/KA/RERA/1250/304/PR/190719/002702
