

PROVIDENT BOTANICO

Construction Updates

February 2025



Dear Esteemed Customer,


Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Botanico. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation.

Team Provident Botanico

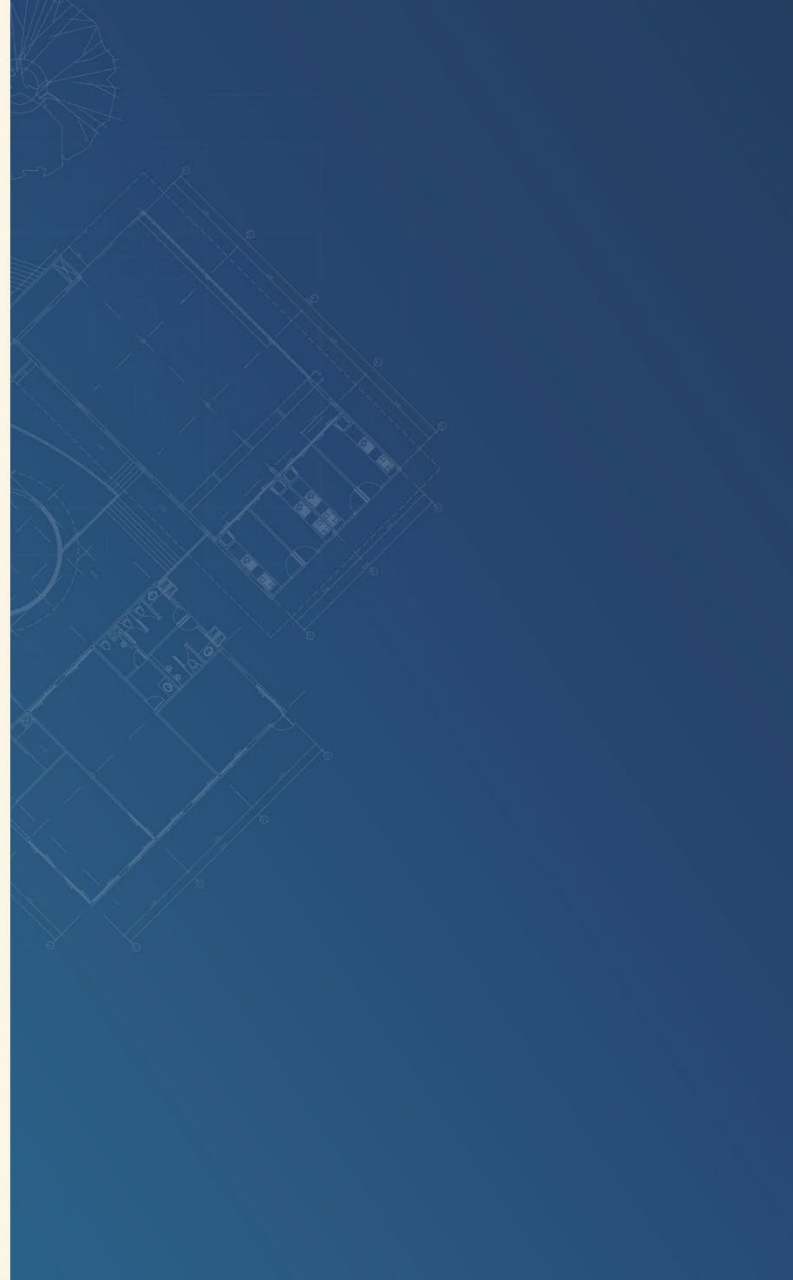



Provident Botanico

Soukya Road, Whitefield



Construction Updates

Overall view

Tower 1



Actual site photograph

TOWER STATUS

- Mass excavation completed.
- ATT & PCC work completed.
- Raft/footing concrete work completed.
- 100% trench raft and wall work completed.
- 100% back filling work completed.
- 100% grade slab PCC work completed.
- 50% grade slab concrete completed.
- 100% ground floor roof slab concrete completed.
- 1st to 2nd floor walls - shuttering & reinforcement work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Mass excavation completed.
- Stilt / ground floor roof slab completed.



UPCOMING CONSTRUCTION MILESTONES

- 2nd floor roof slab concrete completion.

PROGRESS TIMELINE



November 24

December 24

January 25

February 25

Tower 2



Actual site photograph

TOWER STATUS

- Mass excavation completed.
- ATT & PCC work completed.
- Raft/footing concrete work completed.
- 100% walls, column work completed.
- 100% trench raft and wall work completed.
- 100% back filling completed.
- 100% grade slab PCC work completed.
- 50% grade slab concrete completed.
- 80% ground floor roof slab concrete completed balance shuttering & reinforcement work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Mass excavation completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of stilt / ground floor roof slab.

PROGRESS TIMELINE



November 24

December 24

January 25

February 25

Tower 3



Actual site photograph

TOWER STATUS

- Mass excavation completed.
- ATT & PCC work completed.
- Raft/footing concrete work completed.
- Raft, footing cast is completed.
- 100% shear wall and column completed.
- 100% trench raft and wall work completed.
- 100% grade slab PCC work completed.
- 50% grade slab concrete completed.
- 50% ground floor roof slab concrete completed, balance area shuttering and reinforcement work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Mass excavation completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of stilt / ground floor roof slab.

PROGRESS TIMELINE



November 24

December 24

January 25

February 25

Tower 4



Actual site photograph

TOWER STATUS

- Mass excavation completed.
- ATT & PCC work completed.
- Raft/footing concrete work completed.
- 100% shear wall and column completed.
- 100% grade slab PCC work completed.
- 80% grade slab concrete completed.
- 40% ground floor roof slab reinforcement & shuttering work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Mass excavation completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of stilt / ground floor roof slab.

PROGRESS TIMELINE




November 24

December 24

January 25

February 25

Tower 5

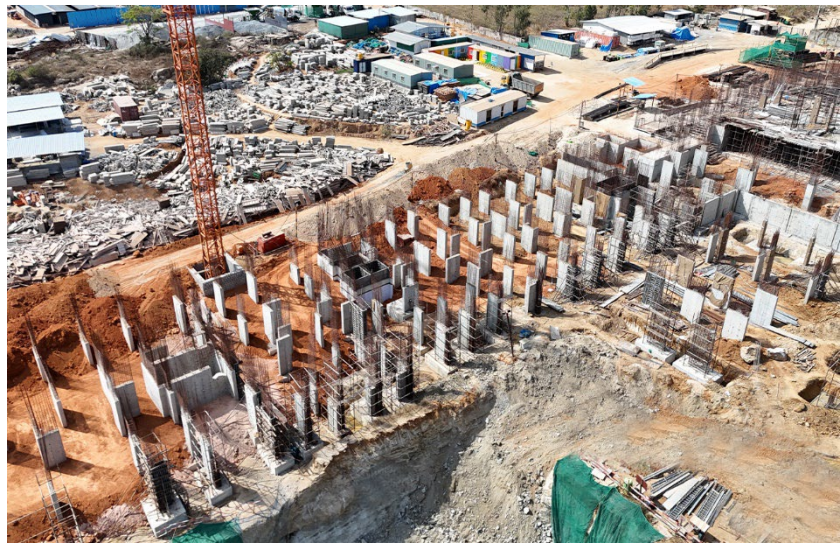

Actual site photograph

TOWER STATUS

- Mass excavation completed.
- ATT & PCC work completed.
- Raft/footing concrete work completed.
- Shear wall and column completed.
- Backfilling work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Mass excavation completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of stilt / ground floor roof slab.

PROGRESS TIMELINE



November 24

December 24

January 25

February 25

Tower 6



Actual site photograph

TOWER STATUS

- Mass excavation completed.
- ATT & PCC work completed.
- Footing work completed.
- Shear wall and column completed.
- Backfilling work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Mass excavation completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of stilt / ground floor roof slab.

PROGRESS TIMELINE



November 24

December 24

January 25

February 25

Tower 7



Actual site photograph

TOWER STATUS

- Mass excavation completed.
- ATT & PCC work completed.
- Raft/footing concrete work completed.
- Shear wall and column casting completed.
- Back filling completed.
- Grade slab PCC completed.
- 100% grade slab PCC work completed.
- 100% basement roof slab completed.
- Ground floor to 1st floor slab shuttering & reinforcement work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Mass excavation completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of stilt / ground floor roof slab.

PROGRESS TIMELINE



November 24

December 24

January 25

February 25

Tower 8



Actual site photograph

TOWER STATUS

- Excavation work completed.
- ATT & PCC work completed.
- Footing / raft concrete completed.
- Column & shear wall concrete completed.
- Basement roof slab shuttering & reinforcement steel work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Mass excavation completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of stilt / ground floor roof slab.

PROGRESS TIMELINE



November 24

December 24

January 25

February 25

Tower 9



Actual site photograph

TOWER STATUS

- Mass excavation completed.
- ATT & PCC work completed.
- Raft/footing concrete work completed.
- Shear wall and column completed.
- Basement roof slab concrete completed.



CONSTRUCTION MILESTONES ACHIEVED

- Mass excavation completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of stilt / ground floor roof slab.

PROGRESS TIMELINE



November 24

December 24

January 25

February 25

STP



Actual site photograph

TOWER STATUS

- Mass excavation completed.
- 98% of excavation completed.
- PCC works in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Mass excavation completed.



UPCOMING CONSTRUCTION MILESTONES

- STP work completion.

PROGRESS TIMELINE



November 24

December 24

January 25

February 25

Clubhouse



Actual site photograph

TOWER STATUS

- Mass excavation completed.
- ATT & PCC work completed.
- Raft/footing concrete work completed
- 70% ground floor roof slab completed, balance area shuttering & reinforcement work in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Mass excavation completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of stilt / ground floor roof slab.

PROGRESS TIMELINE



January 25

February 25

Contact Us



Site Office :

Provident Botanico

Soukya Road, Whitefield, Bengaluru, Karnataka 562114

Regional Office :

Provident Housing Limited

No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-44555544

Email : crm@providenthousing.com (Subject line – Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.providenthousing.com

RERA Registration Number :

RERA Nos.: PRM/KA/RERA/1250/304/PR/210324/006726
